

# Presentation to

# New Commanders

# Mr. Gary Thurston

## March 2000



# Status by Service/Agency

| <b><i>SPS Installed Sites and</i></b> |                     |                     |                     |                     |                     |
|---------------------------------------|---------------------|---------------------|---------------------|---------------------|---------------------|
| <b>Total</b>                          | <b>12/97</b>        | <b>12/98</b>        | <b>12/99</b>        | <b>"12/00"</b>      |                     |
|                                       | <b><u>Users</u></b> | <b><u>Users</u></b> | <b><u>Users</u></b> | <b><u>Users</u></b> | <b><u>Users</u></b> |
| <b>Army</b>                           | <b>0</b>            | <b>1,046</b>        | <b>6,983</b>        | <b>7,500</b>        |                     |
| <b>8,441</b>                          |                     |                     |                     |                     |                     |
| <b>Navy</b>                           | <b>3,186</b>        | <b>6,395</b>        | <b>7,431</b>        | <b>7,700</b>        |                     |
| <b>8,975</b>                          |                     |                     |                     |                     |                     |
| <b>Air Force</b>                      | <b>0</b>            | <b>0</b>            | <b>954</b>          | <b>3,600</b>        |                     |
| <b>7,535</b>                          |                     |                     |                     |                     |                     |
| <b>Marines</b>                        | <b>261</b>          | <b>377</b>          | <b>557</b>          | <b>570</b>          |                     |
| <b>772</b>                            |                     |                     |                     |                     |                     |
| <b>DLSC</b>                           | <b>88 sites</b>     | <b>236 sites</b>    | <b>594 sites</b>    | <b>780 sites</b>    | <b>1,077 sites</b>  |
| <b>1,200</b>                          |                     |                     |                     |                     |                     |
| <b>DCMC</b>                           | <b>0</b>            | <b>0</b>            | <b>0</b>            | <b>0</b>            | <b>0</b>            |
| <b>11,000</b>                         |                     |                     |                     |                     |                     |

Note 1. Reduced users at DES and DCMC with V3.5 who are waiting until V5.1

Continued?

# FY 99 Component Status

*As of 28 December 1999*

| Service                        | Sites      | Users<br>Installed | Users<br>Trained | Traine<br>d/<br>Install | Op<br>Users <sup>1</sup> | Op/<br>Installe<br>d | Op/<br>Trained |
|--------------------------------|------------|--------------------|------------------|-------------------------|--------------------------|----------------------|----------------|
| USA                            | 296        | 6,983              | 5,756            | 82%                     | 6,200                    | 89%                  | 108%           |
| USN                            | 203        | 7,431              | 5,745            | 77%                     | 1,929                    | 26%                  | 34%            |
| USAF                           | 19         | 954                | 1,004            | 105%                    | 645                      | 68%                  | 64%            |
| USMC                           | 35         | 557                | 557              | 100%                    | 371                      | 67%                  | 67%            |
| DLSC                           | 10         | 833                | 449              | 54%                     | 14                       | 2%                   | 3%             |
| DCMC                           | 0          | 0                  | 0                | 0%                      | 0                        | 0%                   | 0%             |
| ODA                            | 31         | 0                  | 0                | 57%                     | 436                      | 61%                  | 107%           |
| <b>Grand Total</b>             | <b>594</b> | <b>17,475</b>      | <b>13,918</b>    | <b>80%</b>              | <b>9,595</b>             | <b>55%</b>           | <b>69%</b>     |
| <b>DELTA</b><br>(Last 90 Days) | <b>114</b> | <b>1,912</b>       | <b>2,749</b>     | <b>•</b>                | <b>3,631</b>             | <b>•</b>             | <b>•</b>       |

1. Component Management Office reporting number of users at FOC or operational.


Sites & Users Installed-  
Users Trained  
Operational Users

PMO Deployment IPRs

- AMS Master Training Schedule & Training DD250's
- CMO Provided Lists

Continued

# Deployed Locations as of 12/00

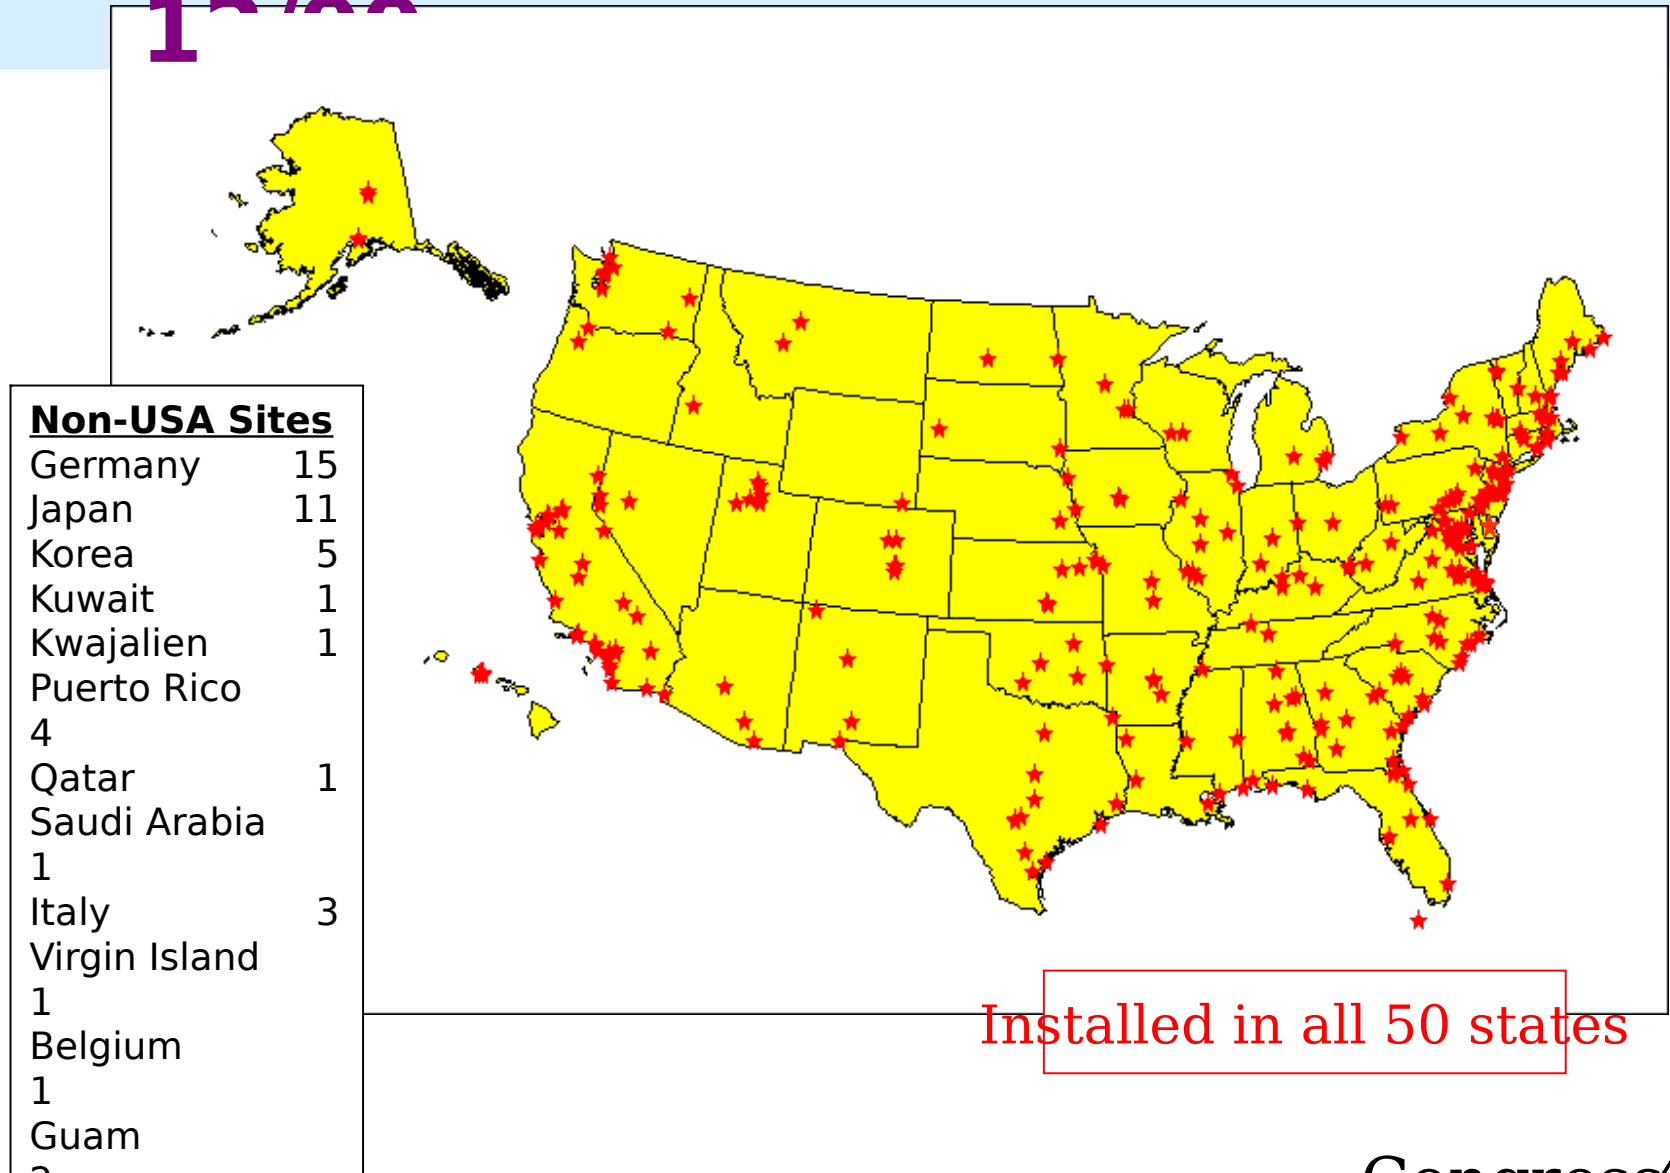


## Non-USA Sites

|               |    |
|---------------|----|
| Germany       | 15 |
| Japan         | 11 |
| Korea         | 5  |
| Kuwait        | 1  |
| Kwajalien     | 1  |
| Puerto Rico   | 4  |
| Qatar         | 1  |
| Saudi Arabia  | 1  |
| Italy         | 3  |
| Virgin Island | 1  |
| Belgium       | 1  |
| Guam          | 2  |

# Deployments to Components

*Installed to Date and Projected to Total = 41,830*

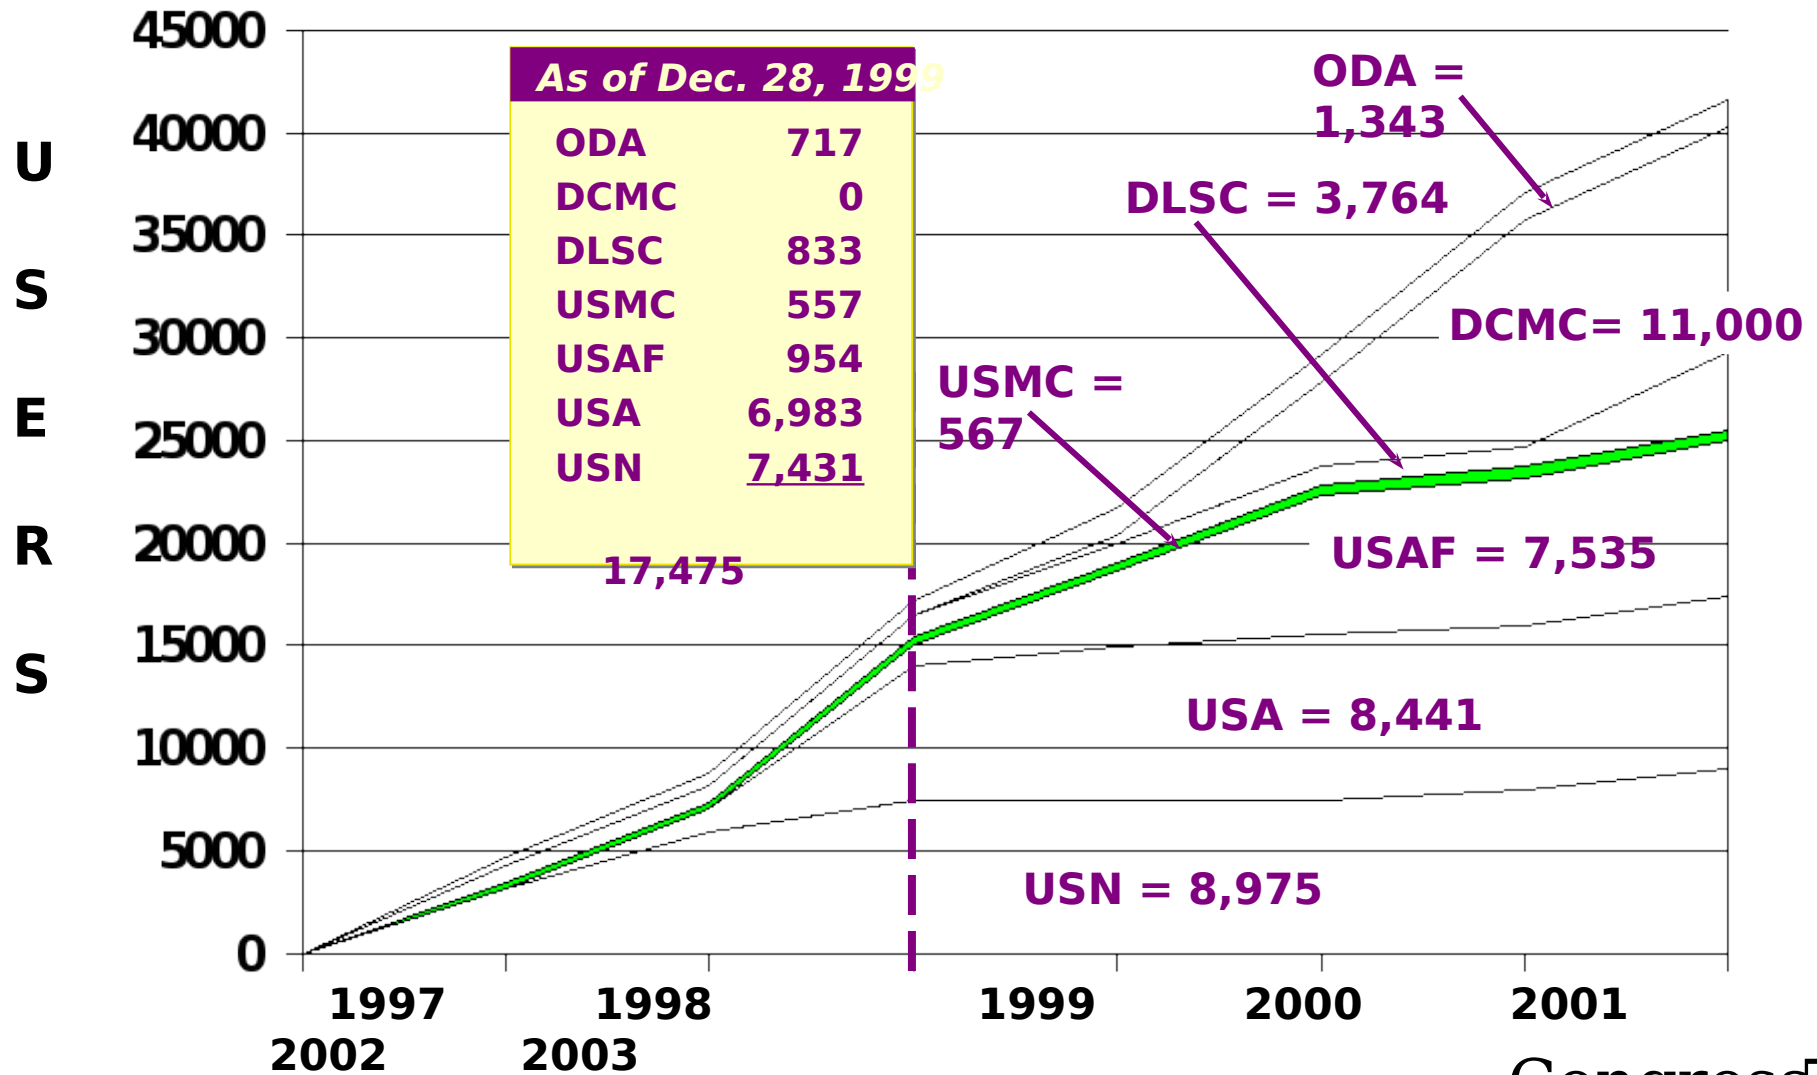

# Deployment Roadmap

## Projected Remaining Legacy Retirements

| FY 1999 |    |    |    | FY 2000 |    |    |    | FY 2001 |    |    |    | FY 2002 |    |    |    | FY 2003 |    |    |    |
|---------|----|----|----|---------|----|----|----|---------|----|----|----|---------|----|----|----|---------|----|----|----|
| Q1      | Q2 | Q3 | Q4 | Q1      | Q2 | Q3 | Q4 | Q1      | Q2 | Q3 | Q4 | Q1      | Q2 | Q3 | Q4 | Q1      | Q2 | Q3 | Q4 |



**SPS  
v4.1**

~~APADE, USMC BCAS, SAACONS, SACS~~

**Quarterly  
Maintenance Releases**



**SPS  
v4.2**



**SPS  
v5.0**



**SPS  
v5.1**

**Post / Camp / Station**

**P/C/S Update**

**SITES: ~811  
USERS: 21,029**

~~BCAS, BOSS~~

**Contract Administration**

**SITES:  
~123  
USERS:  
11,000**

~~MOCAS~~

**MWS**

**SITES:  
~69  
USERS:  
2,222**

~~AMIS  
AMAS  
ConWrite~~

**ICPs**

**SITES:  
~36  
USERS:  
5,633**



~~PADDs  
ITIMP  
ACPS  
DPACS~~

**SPS Deployment Roadmap to  
retire legacy systems and  
achieve operational use for  
all  
procurement users  
by end of FY03**

# Strategy of Shared Responsibilities

PROVIDED BY PMO  
WHO PROVIDES WHAT?

DEPARTMENT / AGENCY FURNISHED

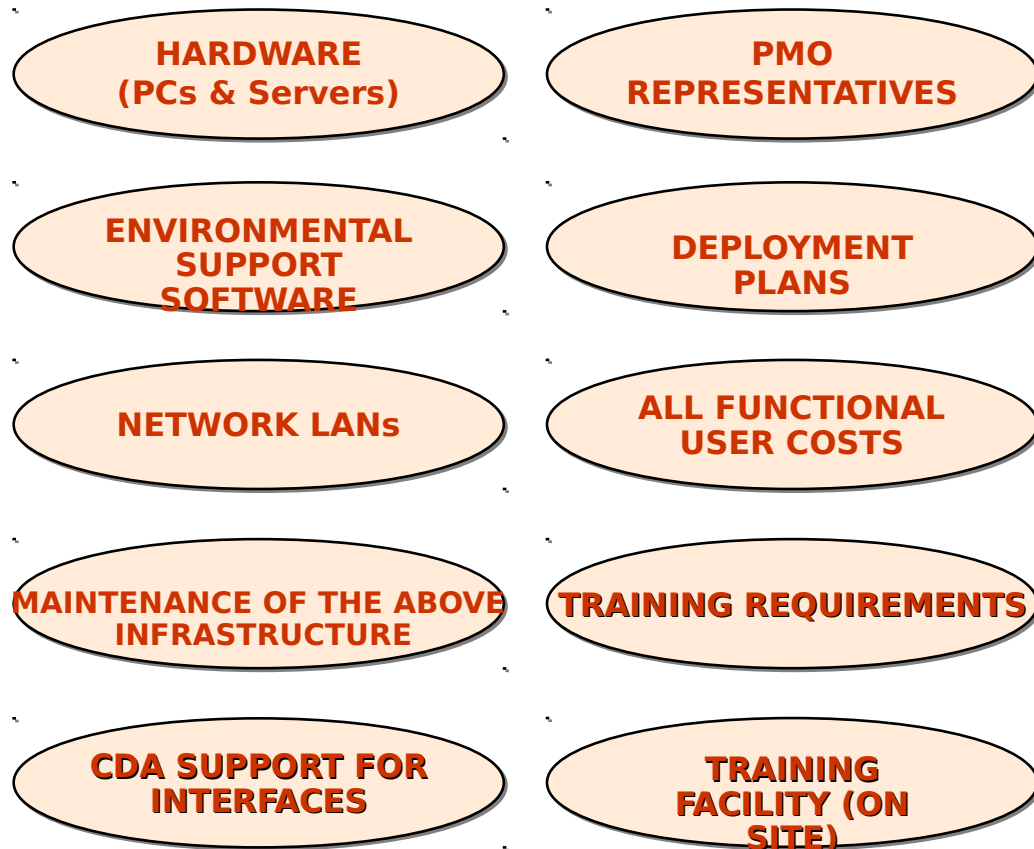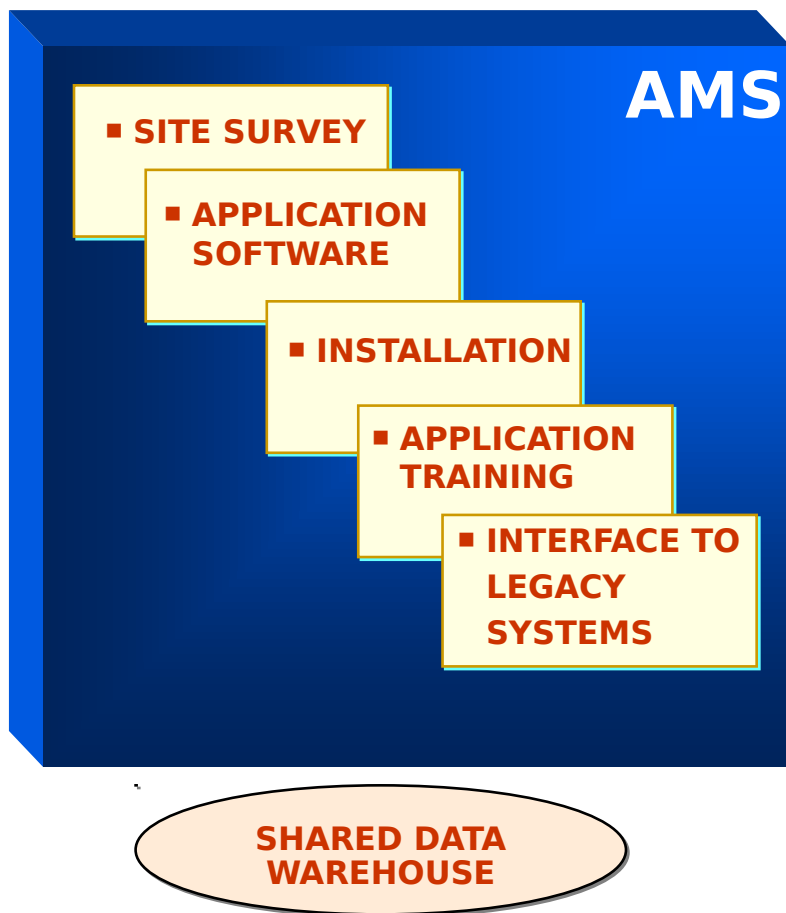




# SPS Vision for the Future

**BEFORE**

**AFTER**

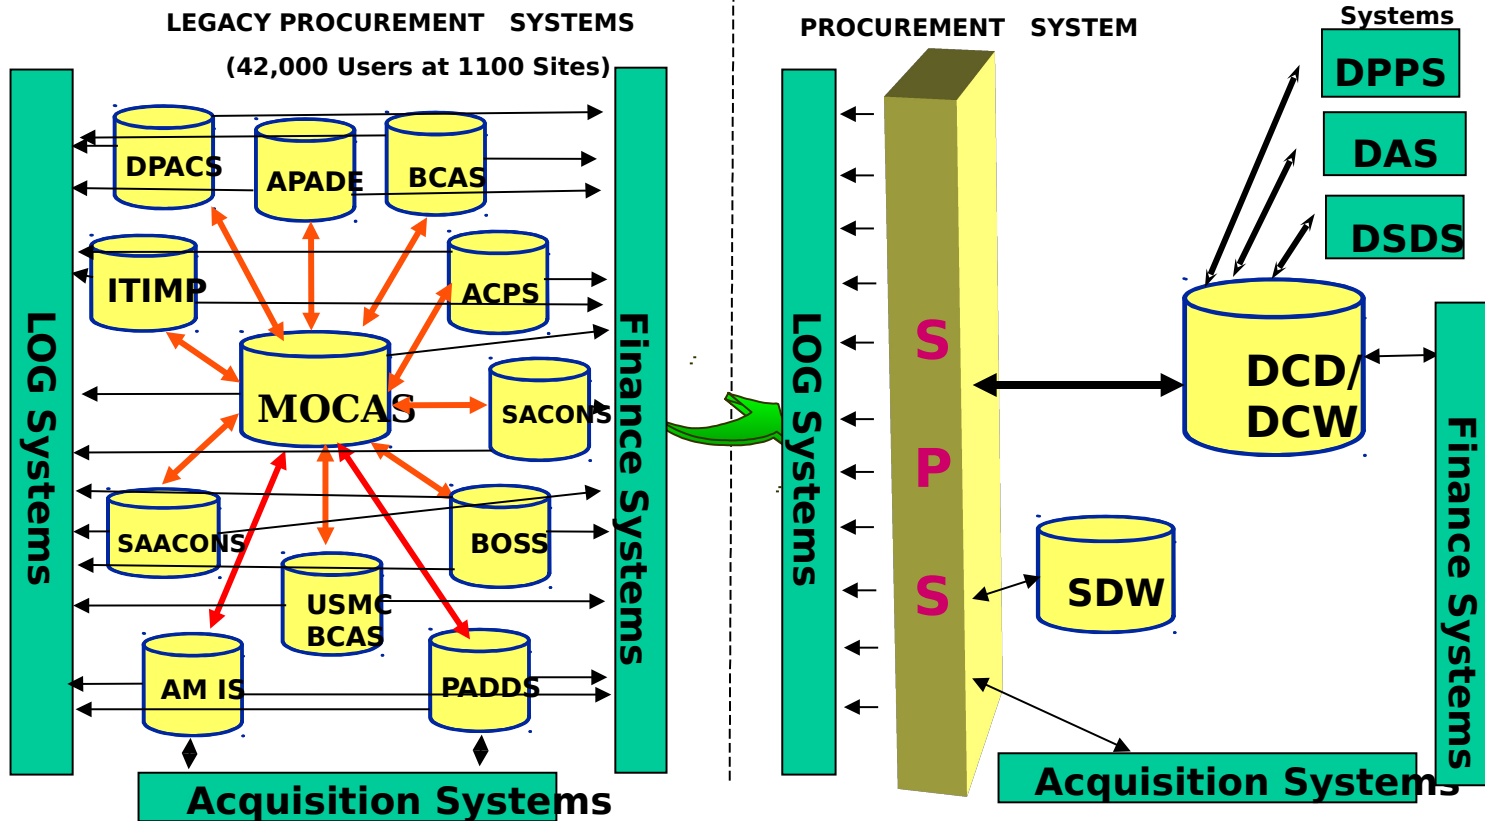



## Summary

**Deployment of SPS continues across DoD with operational use increasing.**

**For Standardization**  
*Software alone isn't the Answer...*

**Leadership & Will Are!!**

# Backups

# Legacy Systems

## ARMY

|                |                                                                           |
|----------------|---------------------------------------------------------------------------|
| <b>SAACONS</b> | <b>Standard Army Automated Contracting System (Base Level)</b>            |
| <b>PADDS</b>   | <b>Procurement Automated Data and Document System (ICP &amp; Weapons)</b> |

## NAVY

|              |                                                                         |
|--------------|-------------------------------------------------------------------------|
| <b>APADE</b> | <b>Automation of Procurement and Accounting Data Entry (Base Level)</b> |
| <b>ITIMP</b> | <b>Integrated Technical Item Management and Procurement (ICP)</b>       |
| <b>AMAS</b>  |                                                                         |

## MARINE CORP

|             |                                                        |
|-------------|--------------------------------------------------------|
| <b>BCAS</b> | <b>Base Contracting Automation System (Base Level)</b> |
|-------------|--------------------------------------------------------|

## AIR FORCE

|                 |                                                            |
|-----------------|------------------------------------------------------------|
| <b>AMIS</b>     | <b>Acquisition Management Information System (Weapons)</b> |
| <b>ACPS</b>     |                                                            |
| <b>BCAS</b>     | <b>Base Contracting Automation System (Base Level)</b>     |
| <b>ConWrite</b> | <b>Contract Writing</b>                                    |

## DLSC

|              |                                                  |
|--------------|--------------------------------------------------|
| <b>DPACS</b> | <b>DLA Pre-Award Contracting System (ICP)</b>    |
| <b>BOSS</b>  | <b>Base Operation Supply System (Base Level)</b> |

## DCMC

|              |                                                                                       |
|--------------|---------------------------------------------------------------------------------------|
| <b>MOCAS</b> | <b>Mechanization of Contract Administration Services (Administration and Payment)</b> |
|--------------|---------------------------------------------------------------------------------------|

## ODAs

|               |                                                           |
|---------------|-----------------------------------------------------------|
| <b>SACONS</b> | <b>Standard Automated Contracting System (Base Level)</b> |
|---------------|-----------------------------------------------------------|

## DFAS

|                |                                                          |
|----------------|----------------------------------------------------------|
| <b>DCD/DCW</b> | <b>DFAS Corporate Database, DFAS Corporate Warehouse</b> |
| <b>CCR</b>     | <b>Central Contractor Registration</b>                   |

# Acronyms and Abbreviations

|                   |                                                  |
|-------------------|--------------------------------------------------|
| <b>ADM</b>        | <b>Acquisition Decision Memorandum</b>           |
| <b>APB</b>        | <b>Acquisition Program Baseline</b>              |
| <b>Components</b> | <b>Military Departments and Defense Agencies</b> |
| <b>DEBX</b>       | <b>Defense Electronic Business Exchange</b>      |
| <b>DFAS</b>       | <b>Defense Finance and Accounting Service</b>    |
| <b>DISA</b>       | <b>Defense Information Systems Agency</b>        |
| <b>DLA</b>        | <b>Defense Logistics Agency</b>                  |
| <b>EDA</b>        | <b>Electronic Document Access</b>                |
| <b>EDI</b>        | <b>Electronic Data Interchange</b>               |
| <b>FOC</b>        | <b>Full Operational Capability</b>               |
| <b>IDIQ</b>       | <b>Indefinite Delivery/Indefinite Quantity</b>   |
| <b>Mil Dep</b>    | <b>Military Departments</b>                      |
| <b>ODA</b>        | <b>Other Defense Agencies</b>                    |
| <b>PC</b>         | <b>Personal Computer</b>                         |
| <b>PDM</b>        | <b>Program Decision Memorandum</b>               |
| <b>POM</b>        | <b>Program Objective Memorandum</b>              |
| <b>PM</b>         | <b>Program Manager</b>                           |
| <b>PMO</b>        | <b>Program Management Office</b>                 |
| <b>SDW</b>        | <b>Shared Data Warehouse</b>                     |
| <b>SPS</b>        | <b>Standard Procurement System</b>               |
| <b>SPS-I</b>      | <b>SPS-Interface</b>                             |
| <b>VAN</b>        | <b>Value Added Network</b>                       |
